



New Seguin High School Weekly Report May 4, 2017

Project Name: New Seguin High School
Arch/Engineer: ERO Architects
Construction Program Manager: Broaddus & Associates
Contractor: Bartlett Cocke/Koehler
Current Phase: Construction Administration

1) CURRENT PROJECT STATUS

- a. Gymnasiums and Athletic Areas
 - BC-K will send out a request for architectural punch, next week, and to be scheduled for Wednesday.
- b. Performing Arts Center/Fine Arts/Choir
 - Working towards an above ceiling punch, to be scheduled next week
 - On-going installation of handrails in Auditorium
 - Getting ready to start installing stage flooring and Black Box
 - Continuing with MEP work above ceiling
 - Getting ready to start lay-in ceilings
- c. Administration/General Classrooms
 - Design team was doing a final review and sign-off on above ceiling punch corrections
 - On-going finishes
 - Conditioned air should be on sometime next week
 - Going to start lay-in ceiling tile installation
 - BC-K is preparing to begin their architectural punch
- d. General Classrooms / CTE
 - Working above ceiling punch-list work on levels 2 & 3 in area E
 - Clean up in progress
 - CTE area is progressing
- e. Cafeteria/Kitchen/Library
 - Working above ceiling punch-list work on levels 2 & 3
 - Working on TF&T
 - Ceiling grid installed at high areas
 - Exterior plaster at front entry tower in progress
 - Installing fixtures



New Seguin High School Weekly Report May 4, 2017

Project Name: New Seguin High School
Arch/Engineer: ERO Architects
Construction Program Manager: Broaddus & Associates
Contractor: Bartlett Cocke/Koehler
Current Phase: Construction Administration

- Installing some acoustical wall panel framing brackets in Cafeteria
- Working above ceiling punch-list work
- Some panels need to be replaced on the walk-in cooler – not working on this presently
- Coordinating installation of Ansel System
- End of May or first of June for equipment start-up

f. General

- Continued production
- Working above ceiling punch-list work
- Some panels need to be replaced on the walk-in cooler – not working on this presently
- Coordinating installation of Ansel System
- End of May or first of June for equipment start-up
- Making progress on site work
- Connex containers have been moved
- Starting work on north parking lot on 4/27/2017
- Courtyard curbs are poured, and getting ready for flatwork
- Will begin flatwork on west side of CTE, and west & north sides of Freshman Center, once completed with courtyard.
- Coaches portables will be removed next week

2) SCHEDULE

BC-K reported that weather has been good. The total rain event days to-date, still stands at 58 days of limited production, and 32 (12 site related only) rain days of zero production. Project is at 85% completion, as of this week, and on target to meet original schedule.



New Seguin High School Weekly Report May 4, 2017

Project Name: New Seguin High School
Arch/Engineer: ERO Architects
Construction Program Manager: Broaddus & Associates
Contractor: Bartlett Cocke/Koehler
Current Phase: Construction Administration



NORTH VIEW OF CAMPUS

Cleared connex storage units, and preparing to work on parking lot.



New Seguin High School Weekly Report May 4, 2017

Project Name: New Seguin High School
Arch/Engineer: ERO Architects
Construction Program Manager: Broaddus & Associates
Contractor: Bartlett Cocke/Koehler
Current Phase: Construction Administration



ADMINISTRATION AND CLASSROOMS

Working on finishes, prepping for flooring finishes at main atrium.



New Seguin High School Weekly Report May 4, 2017

Project Name: New Seguin High School
Arch/Engineer: ERO Architects
Construction Program Manager: Broaddus & Associates
Contractor: Bartlett Cocke/Koehler
Current Phase: Construction Administration



INTERIORS

Miscellaneous finish work at main entrance atrium in area F (left photo). Working on finishes in PAC lobby in area A (right photo).



New Seguin High School Weekly Report May 4, 2017

Project Name: New Seguin High School
Arch/Engineer: ERO Architects
Construction Program Manager: Broaddus & Associates
Contractor: Bartlett Cocke/Koehler
Current Phase: Construction Administration



ATHLETICS

Working on final finishing coats of wood floor in auxiliary gym (top photo). Main athletics corridor ready for architectural punch. (bottom photo).



New Seguin High School Weekly Report May 4, 2017

Project Name: New Seguin High School
Arch/Engineer: ERO Architects
Construction Program Manager: Broaddus & Associates
Contractor: Bartlett Cocke/Koehler
Current Phase: Construction Administration



CAFETERIA/KITCHEN – Working on storefront system at the entrance to the cafeteria. (top photo). Above ceiling work at serving lines (bottom photo).



New Seguin High School Weekly Report May 4, 2017

Project Name: New Seguin High School
Arch/Engineer: ERO Architects
Construction Program Manager: Broaddus & Associates
Contractor: Bartlett Cocke/Koehler
Current Phase: Construction Administration




LIBRARY

Working on drywall, and misc. MEP items.



New Seguin High School Weekly Report May 4, 2017

Project Name: New Seguin High School
Arch/Engineer: ERO Architects
Construction Program Manager: Broaddus & Associates
Contractor: Bartlett Cocke/Koehler
Current Phase: Construction Administration

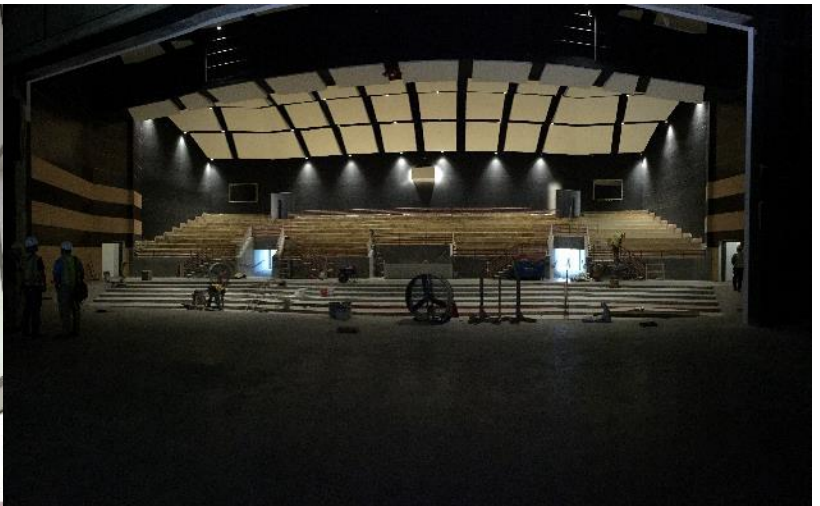

PERFORMING ARTS CENTER

Prepping for painting of the rails, and clean-up at Lobby (left photo). On-going railing installation, and staining of auditorium floors. (right photo).



New Seguin High School Weekly Report May 4, 2017

Project Name: New Seguin High School
Arch/Engineer: ERO Architects
Construction Program Manager: Broaddus & Associates
Contractor: Bartlett Cocke/Koehler
Current Phase: Construction Administration



SITWORK

Driveway work, and grading at northwest corner of Area A and Freshman Center. (top photo).
Driveway complete at bus-loop, and starting parking lot work at northeast side campus. (top right photo).
