




F.A. NUNNELLY

GENERAL CONTRACTOR

ID	Task Name	Start	Finish	Aug '19	Sep '19	Oct '19	Nov '19	Dec '19	Jan '20	Feb '20	Mar '20	Apr '20	May '20	Jun '20	Jul '20	Aug '20	Se				
0	19-010 Matador Stadium - Working Schedule	Mon 8/5/19	Mon 8/17/20	0%																	
1	General Conditions	Mon 8/5/19	Tue 10/1/19	0%																	
7	Submittals / Long Lead Procurement	Mon 8/5/19	Fri 12/6/19	0%																	
15	Mobilize on Site	Mon 8/19/19	Thu 11/21/19	0%																	
16	Submit demo notification to State	Mon 8/19/19	Fri 8/30/19	0%																	
17	Install SWPPP - Phase I	Mon 9/16/19	Tue 9/17/19	0%																	
18	Install SWPPP - Phase II	Mon 11/18/19	Tue 11/19/19	0%																	
19	Install temp services	Wed 9/18/19	Thu 9/19/19	0%																	
20	Set up site office	Fri 9/20/19	Tue 9/24/19	0%																	
21	Set line and grade benchmarks	Wed 9/25/19	Fri 9/27/19	0%																	
22	Prepare site - lay down yard and temporary fencing - Visitor	Mon 9/30/19	Tue 10/1/19	0%																	
23	Prepare site - lay down yard and temporary fencing - Home	Wed 11/20/19	Thu 11/21/19	0%																	
24	Site Grading and Utilities	Mon 9/16/19	Fri 2/14/20	0%																	
25	Disconnect existing utilities	Mon 9/16/19	Tue 9/17/19	0%																	
26	Phase I Demo and Haul off - Visitor Side Bleachers, Concessions, etc.	Wed 9/18/19	Tue 10/1/19	0%																	
27	COMPLETE PHASE I DEMO	Tue 10/1/19	Tue 10/1/19	10/1																	
28	Phase II Demo and haul off- Home Side Bleachers, Concessions, etc.	Mon 12/2/19	Wed 12/25/19	0%																	
29	COMPLETE PHASE II DEMO	Fri 1/10/20	Fri 1/10/20	1/10																	
30	Phase I - Rough grade site (cut and fill)	Wed 10/2/19	Tue 10/15/19	0%																	
31	Phase II - Rough grade site (cut and fill)	Wed 12/25/19	Wed 1/15/20	0%																	
32	Install storm drainage	Wed 1/15/20	Wed 1/29/20	0%																	
33	Install sanitary sewer	Wed 1/29/20	Fri 2/7/20	0%																	
34	Detention pond improvement	Wed 1/29/20	Fri 2/7/20	0%																	
35	Install fire line, domestic water line	Mon 2/10/20	Fri 2/14/20	0%																	
36	Building pad for Visitor Concession, Ticket Booth	Wed 10/16/19	Tue 10/22/19	0%																	
37	Building pad for Home Concession, Ticket Booth	Wed 1/15/20	Wed 1/29/20	0%																	
38	Site Paving, Site Finishes	Wed 1/29/20	Thu 6/11/20	0%																	
39	Piers / footings for Grandstands - Visitor.	Wed 1/29/20	Fri 2/7/20	0%																	

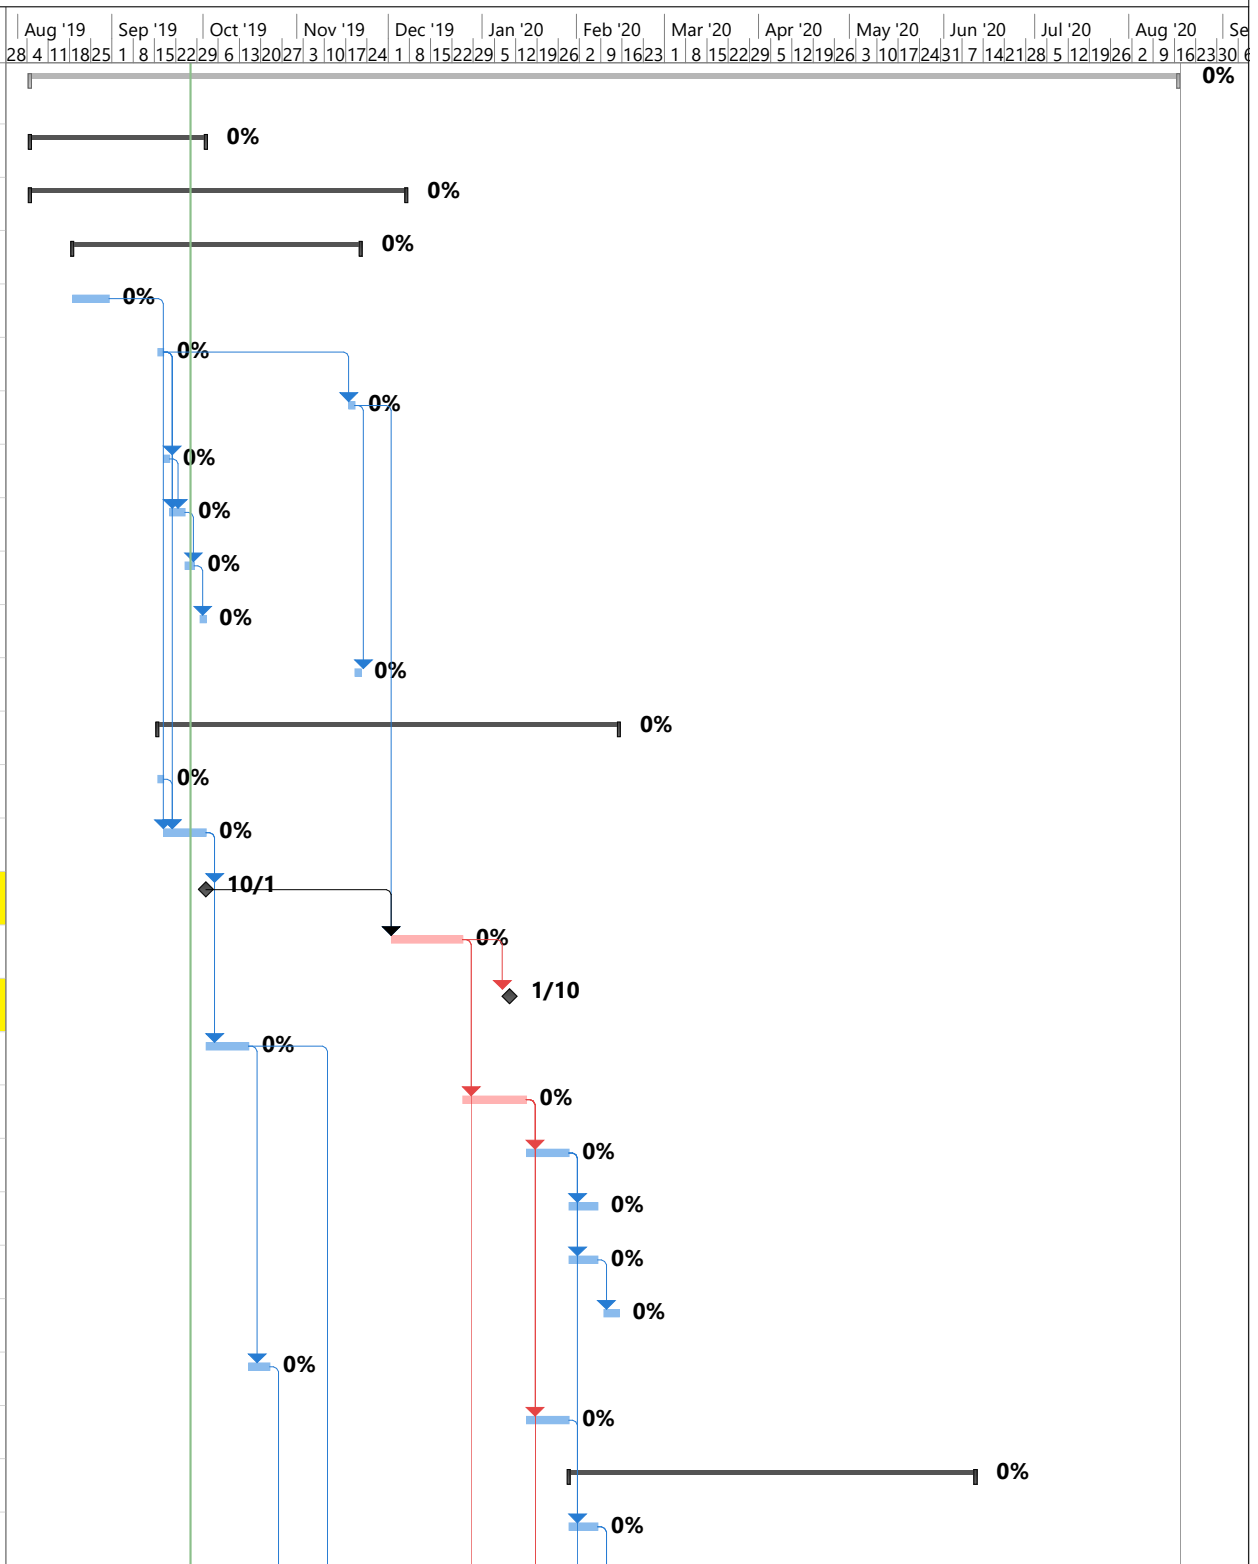




F.A. NUNNELLY

GENERAL CONTRACTOR

ID	Task Name	Start	Finish	Aug '19	Sep '19	Oct '19	Nov '19	Dec '19	Jan '20	Feb '20	Mar '20	Apr '20	May '20	Jun '20	Jul '20	Aug '20	Se
40	Piers / footings for Grandstands - Home.	Mon 2/10/20	Fri 2/21/20								0%						
41	Erect Grandstands - Visitor.	Fri 2/21/20	Fri 4/10/20								0%						
42	Erect Grandstands - Home.	Thu 3/12/20	Wed 5/13/20								0%						
43	COMPLETE GRANDSTANDS	Wed 5/13/20	Wed 5/13/20								0%						
44	Prep subgrade for concrete flatwork at grandstands - Visitor.	Mon 2/10/20	Wed 2/19/20								0%						
45	Prep subgrade for concrete flatwork at grandstands - Home.	Mon 2/24/20	Fri 3/6/20								0%						
46	Prep subgrade for site concrete - all areas outside grandstands.	Wed 5/20/20	Wed 6/3/20								0%						
47	Place site concrete at grandstands - Visitor.	Wed 2/19/20	Fri 2/21/20								0%						
48	Place site concrete at grandstands - Home.	Mon 3/9/20	Wed 3/11/20								0%						
49	Form, reinforce, place site concrete - all areas outside grandstands.	Thu 3/12/20	Wed 4/8/20								0%						
50	Sawcutting of site concrete flatwork.	Thu 4/9/20	Wed 4/15/20								0%						
51	Prep subgrade for asphalt paving	Wed 5/20/20	Tue 5/26/20								0%						
52	Place asphalt paving	Tue 5/26/20	Thu 5/28/20								0%						
53	Landscape	Thu 4/9/20	Wed 4/22/20								0%						
54	Install new site fencing, gates	Thu 4/9/20	Wed 5/6/20								0%						
55	Site Lighting	Thu 2/13/20	Thu 2/27/20								0%						
56	Stone Bollards	Thu 4/9/20	Mon 4/13/20								0%						
57	Flag poles	Thu 4/9/20	Mon 4/13/20								0%						
58	Exterior Signage	Thu 5/28/20	Thu 6/11/20								0%						
59	Field and Track	Wed 12/25/19	Thu 6/25/20								0%						
60	Grade / prep / haul off track and field	Wed 12/25/19	Fri 1/3/20								0%						
61	Place subgrade / fill at track and field	Mon 1/6/20	Wed 2/26/20								0%						
62	Inspection of subgrade / mobilize Field Turf subcontractor	Wed 2/26/20	Wed 3/4/20								0%						
63	COMPLETE TRACK AND FIELD SUBGRADE	Wed 3/4/20	Wed 3/4/20								0%						
64	Place concrete curbs around track / field	Wed 3/4/20	Fri 3/20/20								0%						
65	Dynamic Base (geotextile, drainage, stone, goal posts)	Mon 3/23/20	Wed 4/8/20								0%						
66	Running Track and flex base pave	Wed 4/8/20	Fri 4/24/20								0%						
67	Asphalt cure time	Mon 4/27/20	Wed 5/20/20								0%						
68	Synthetic Turf Installation	Mon 4/27/20	Fri 5/22/20								0%						

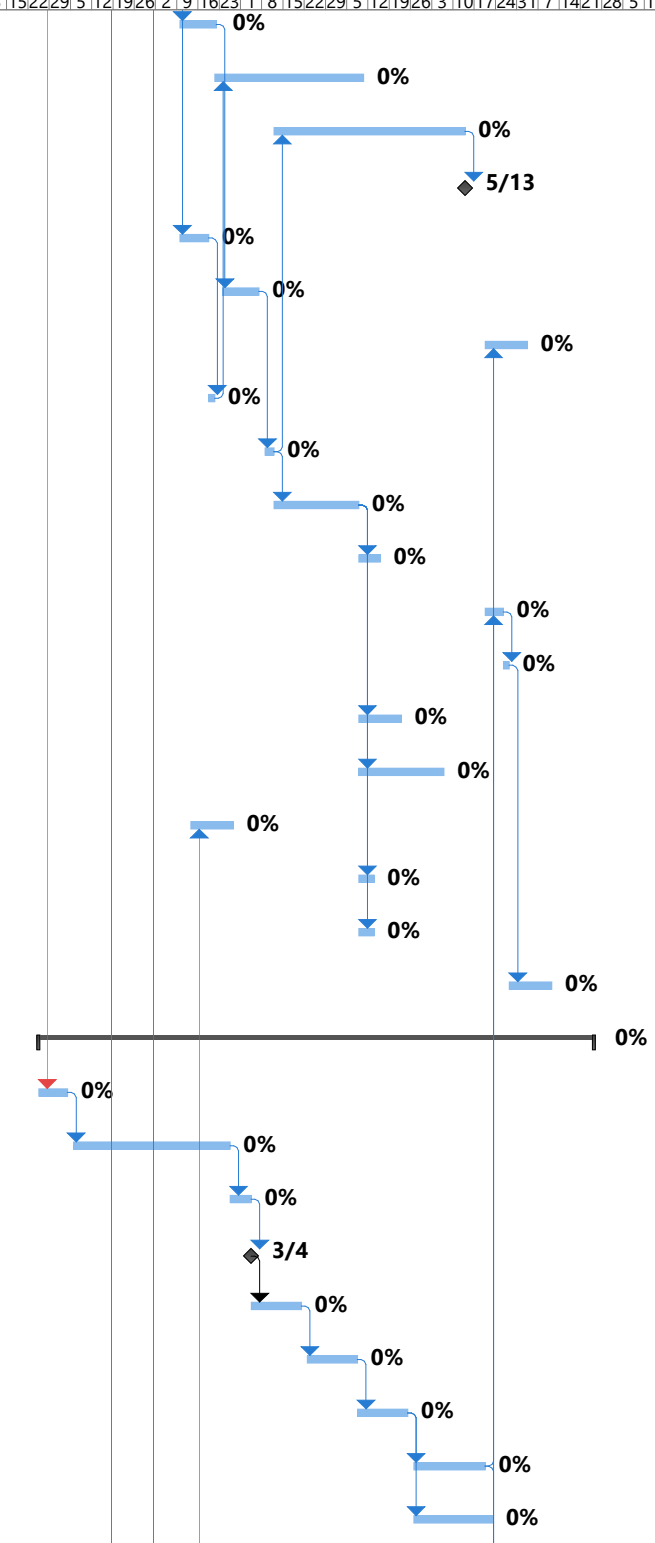




F.A. NUNNELLY

GENERAL CONTRACTOR

ID	Task Name	Start	Finish	Aug '19	Sep '19	Oct '19	Nov '19	Dec '19	Jan '20	Feb '20	Mar '20	Apr '20	May '20	Jun '20	Jul '20	Aug '20	Se
69	Synthetic Track Installation	Wed 5/20/20	Wed 6/17/20														
70	Runways, high jumps	Wed 6/17/20	Mon 6/22/20														
71	COMPLETE TRACK AND FIELD	Thu 6/25/20	Thu 6/25/20														
72	Cleanup field and track	Mon 6/22/20	Thu 6/25/20														
73	Foundations	Wed 10/23/19	Tue 4/28/20														
74	Visitor Concession & Ticket Booth - Excavate foundations	Fri 11/15/19	Fri 11/29/19														
75	Home Concession & Ticket Booth - Excavate foundations	Mon 3/16/20	Fri 4/3/20														
76	PHASE I - VISITOR BUILDING FOUNDATIONS	Fri 11/29/19	Fri 11/29/19														
77	Plumbing rough - Visitor Concession	Wed 10/23/19	Fri 11/15/19														
78	Form, reinforce, place building foundations for Visitor Concession and Ticket Booth	Fri 11/15/19	Tue 12/10/19														
79	PHASE II - HOME BUILDING FOUNDATIONS	Fri 3/13/20	Fri 3/13/20														
80	Plumbing rough - Home Concession	Wed 1/29/20	Fri 3/13/20														
81	Form, reinforce, place building foundations for Home Concession and Ticket Booth	Mon 3/16/20	Fri 4/17/20														
82	Cure Concrete for foundation	Wed 12/11/19	Fri 12/13/19														
83	Cure Concrete for foundation	Mon 4/20/20	Wed 4/22/20														
84	PRESS BOX FOUNDATION	Tue 1/28/20	Tue 1/28/20														
85	Pressbox drilled piers	Wed 1/15/20	Tue 1/28/20														
86	Pressbox beams, footings, walls.	Tue 1/28/20	Tue 2/11/20														
87	Visitor - place piers and foundations for grandstands	Mon 11/11/19	Fri 11/22/19														
88	Home - place piers and foundations for grandstands	Mon 11/25/19	Fri 12/13/19														
89	Excavate elevator pit	Mon 4/6/20	Fri 4/10/20														
90	Rough-in electric and plumbing in elevator	Mon 4/13/20	Thu 4/16/20														
91	Form elevator pit and walls	Fri 4/17/20	Wed 4/22/20														
92	Pour concrete elevator walls / floor	Thu 4/23/20	Thu 4/23/20														
93	Cure elevator wall concrete	Fri 4/24/20	Tue 4/28/20														
94	Drill Piers for screen wall	Tue 1/28/20	Thu 2/6/20														
95	Site Lighting foundations	Thu 2/6/20	Thu 2/13/20														
96	Footing / beam for screen wall	Thu 2/13/20	Thu 2/20/20														
97	Masonry Work	Wed 12/11/19	Wed 5/27/20														

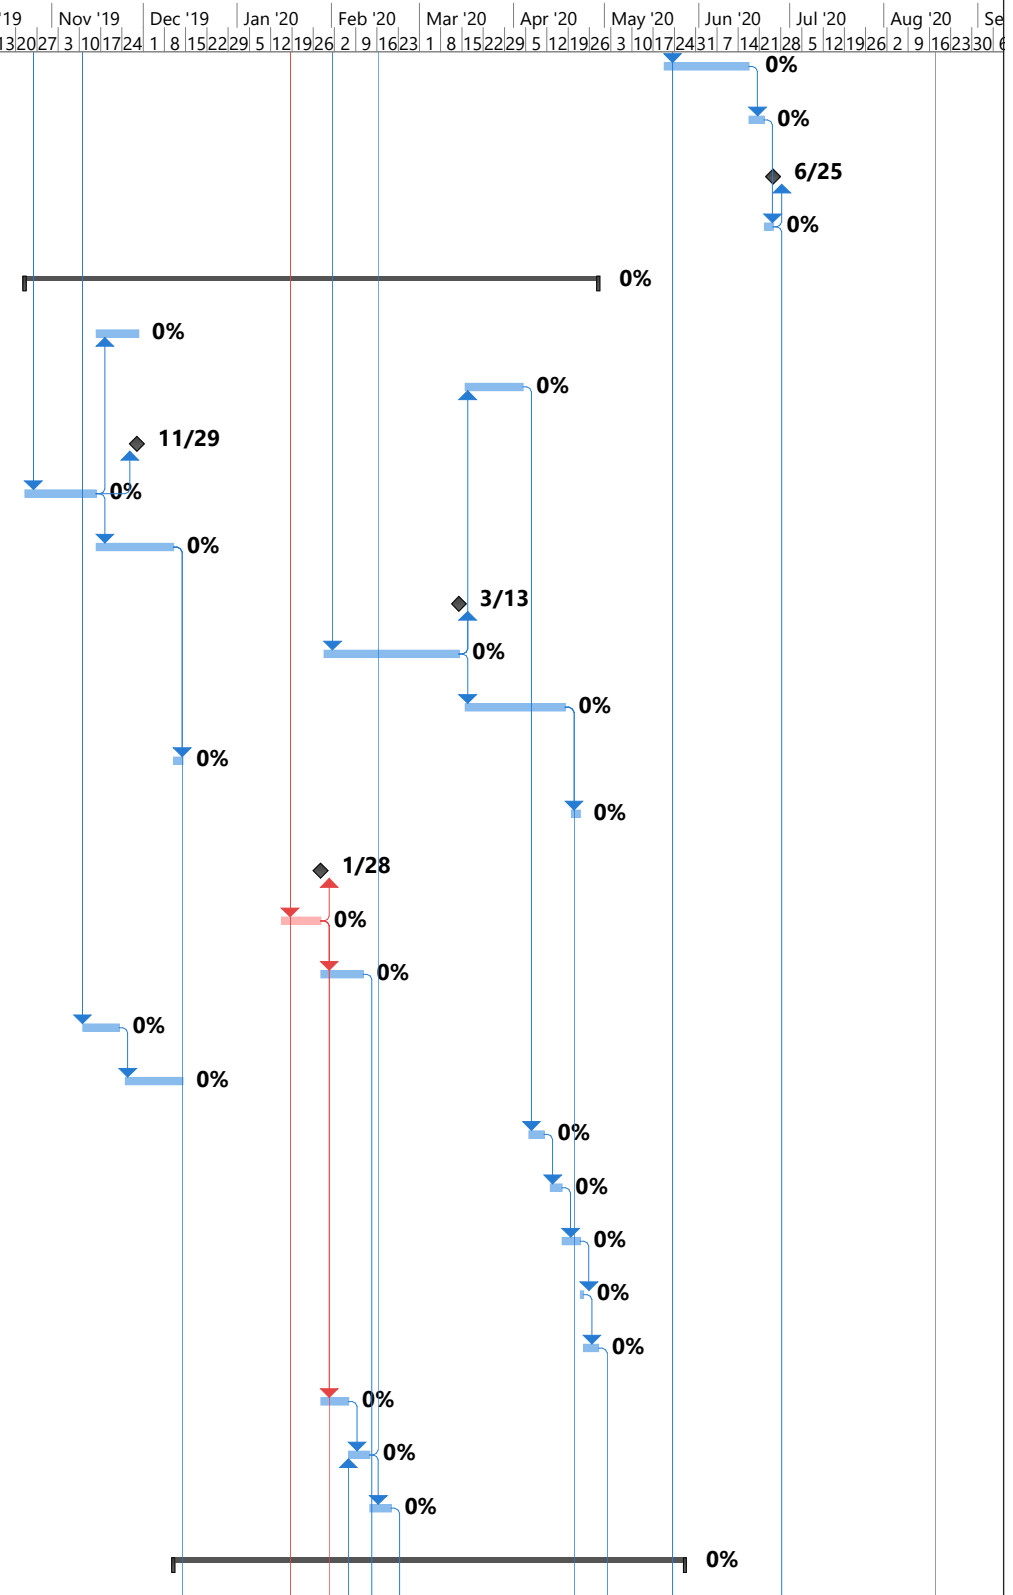



F.A. NUNNELLY

GENERAL CONTRACTOR


ID	Task Name	Start	Finish	Aug '19	Sep '19	Oct '19	Nov '19	Dec '19	Jan '20	Feb '20	Mar '20	Apr '20	May '20	Jun '20	Jul '20	Aug '20	Se
98	CMU at Visitor Concession and Ticket	Wed 12/11/19	Fri 12/20/19						0%								
99	CMU at Home Concession and Ticket	Mon 4/20/20	Fri 5/1/20										0%				
100	CMU at elevator shaft	Wed 4/29/20	Tue 5/5/20										0%				
101	CMU at screen wall	Thu 2/20/20	Thu 3/5/20								0%						
102	CMU at Press Box	Tue 2/11/20	Tue 2/25/20							0%							
103	4" Masonry Veneer	Mon 5/11/20	Wed 5/20/20											0%			
104	COMPLETE MASONRY	Wed 5/20/20	Wed 5/20/20											5/20			
105	Clean masonry	Wed 5/20/20	Wed 5/27/20											0%			
106	Steel Erection	Fri 12/20/19	Wed 5/13/20											0%			
107	Erect steel - Visitor Concession and Ticket Booth	Fri 12/20/19	Fri 12/27/19						0%								
108	Erect steel - Home Concession and Ticket Booth	Mon 5/4/20	Wed 5/13/20											0%			
109	Erect steel - Press Box	Tue 1/28/20	Tue 3/3/20							0%							
110	Install stairs and miscellaneous iron railing	Tue 3/3/20	Tue 3/10/20							0%							
111	Touch-up paint on steel	Tue 3/10/20	Fri 3/13/20							0%							
112	Concrete roof over metal decking	Fri 12/27/19	Wed 5/20/20											0%			
113	Concrete at metal decking - Visitor	Fri 12/27/19	Fri 1/3/20						0%								
114	Concrete at metal decking - Home	Wed 5/13/20	Wed 5/20/20											0%			
115	Rough Carpentry	Thu 3/12/20	Thu 3/26/20											0%			
116	Framing at Press Box	Thu 3/12/20	Thu 3/26/20											0%			
117	Roofing and Moisture Protection	Tue 3/3/20	Wed 6/17/20											0%			
118	Install modified bitumen roofing	Wed 5/20/20	Fri 5/29/20											0%			
119	Parapet caps	Mon 6/1/20	Fri 6/5/20											0%			
120	Set rooftop equipment	Mon 6/1/20	Fri 6/12/20											0%			
121	SSMR at press box	Tue 3/3/20	Thu 3/12/20							0%							
122	Spray Applied Insulation at structural steel	Tue 3/3/20	Tue 3/10/20							0%							
123	Gutters / downspouts	Mon 6/8/20	Wed 6/17/20											0%			
124	Metal Panels	Thu 5/7/20	Thu 6/4/20											0%			
125	Insulation and waterproofing at CMU walls	Mon 5/4/20	Fri 5/8/20											0%			
126	Doors and Windows	Wed 12/11/19	Tue 6/16/20											0%			



F.A. NUNNELLY

GENERAL CONTRACTOR

ID	Task Name	Start	Finish	Aug '19	Sep '19	Oct '19	Nov '19	Dec '19	Jan '20	Feb '20	Mar '20	Apr '20	May '20	Jun '20	Jul '20	Aug '20	Se
127	HM frames at Visitor	Wed 12/11/19	Fri 12/13/19					0%									
128	HM frames at Home	Mon 4/20/20	Wed 4/22/20										0%				
129	Install window wall aluminum and glass at Press Box	Thu 3/26/20	Thu 5/7/20										0%				
130	Install windows at Concessions and Ticket Booth	Wed 5/20/20	Wed 5/27/20											0%			
131	Install Overhead Doors at Concessions	Wed 5/27/20	Wed 6/3/20											0%			
132	Install interior doors and hardware	Thu 6/4/20	Tue 6/16/20												0%		
133	Building Finishes	Thu 4/30/20	Thu 7/2/20														
134	SS Countertops	Tue 6/16/20	Tue 6/23/20												0%		
135	Drywall at Press Box	Thu 4/30/20	Thu 5/7/20												0%		
136	Install millwork and wood trim	Thu 5/7/20	Thu 5/14/20												0%		
137	Paint walls	Thu 5/14/20	Thu 6/4/20												0%		
138	Install ceiling grid	Thu 6/4/20	Thu 6/18/20												0%		
139	Install ceiling tile	Thu 6/18/20	Thu 7/2/20												0%		
140	Install flooring	Thu 5/7/20	Thu 6/4/20												0%		
141	Elevators	Mon 6/1/20	Fri 7/24/20														
142	Set elevator equipment in shafts	Mon 6/1/20	Fri 6/26/20												0%		
143	Set equipment in mechanical room	Mon 6/29/20	Fri 7/10/20												0%		
144	COMPLETE ELEVATOR	Fri 7/24/20	Fri 7/24/20														
145	Test and align doors and equipment	Mon 7/13/20	Fri 7/24/20												0%		
146	Plumbing	Thu 3/26/20	Wed 6/17/20														
147	Rough-in plumbing in CMU wall	Mon 5/4/20	Fri 5/22/20												0%		
148	Rough-in plumbing in drywall walls	Thu 3/26/20	Thu 4/2/20												0%		
149	Fire Sprinkler	Wed 5/13/20	Wed 5/27/20												0%		
150	Set plumbing fixtures and trim - Visitor	Mon 5/25/20	Fri 6/5/20												0%		
151	Set plumbing fixtures and trim - Home	Mon 6/8/20	Wed 6/10/20												0%		
152	Flush, test, and clean piping and fixtures	Thu 6/11/20	Wed 6/17/20												0%		
153	Electrical	Wed 1/15/20	Thu 7/2/20														
154	Rough-in electrical in masonry walls	Mon 5/25/20	Fri 6/19/20												0%		
155	Rough-in electrical in drywall walls	Thu 4/2/20	Thu 4/30/20												0%		

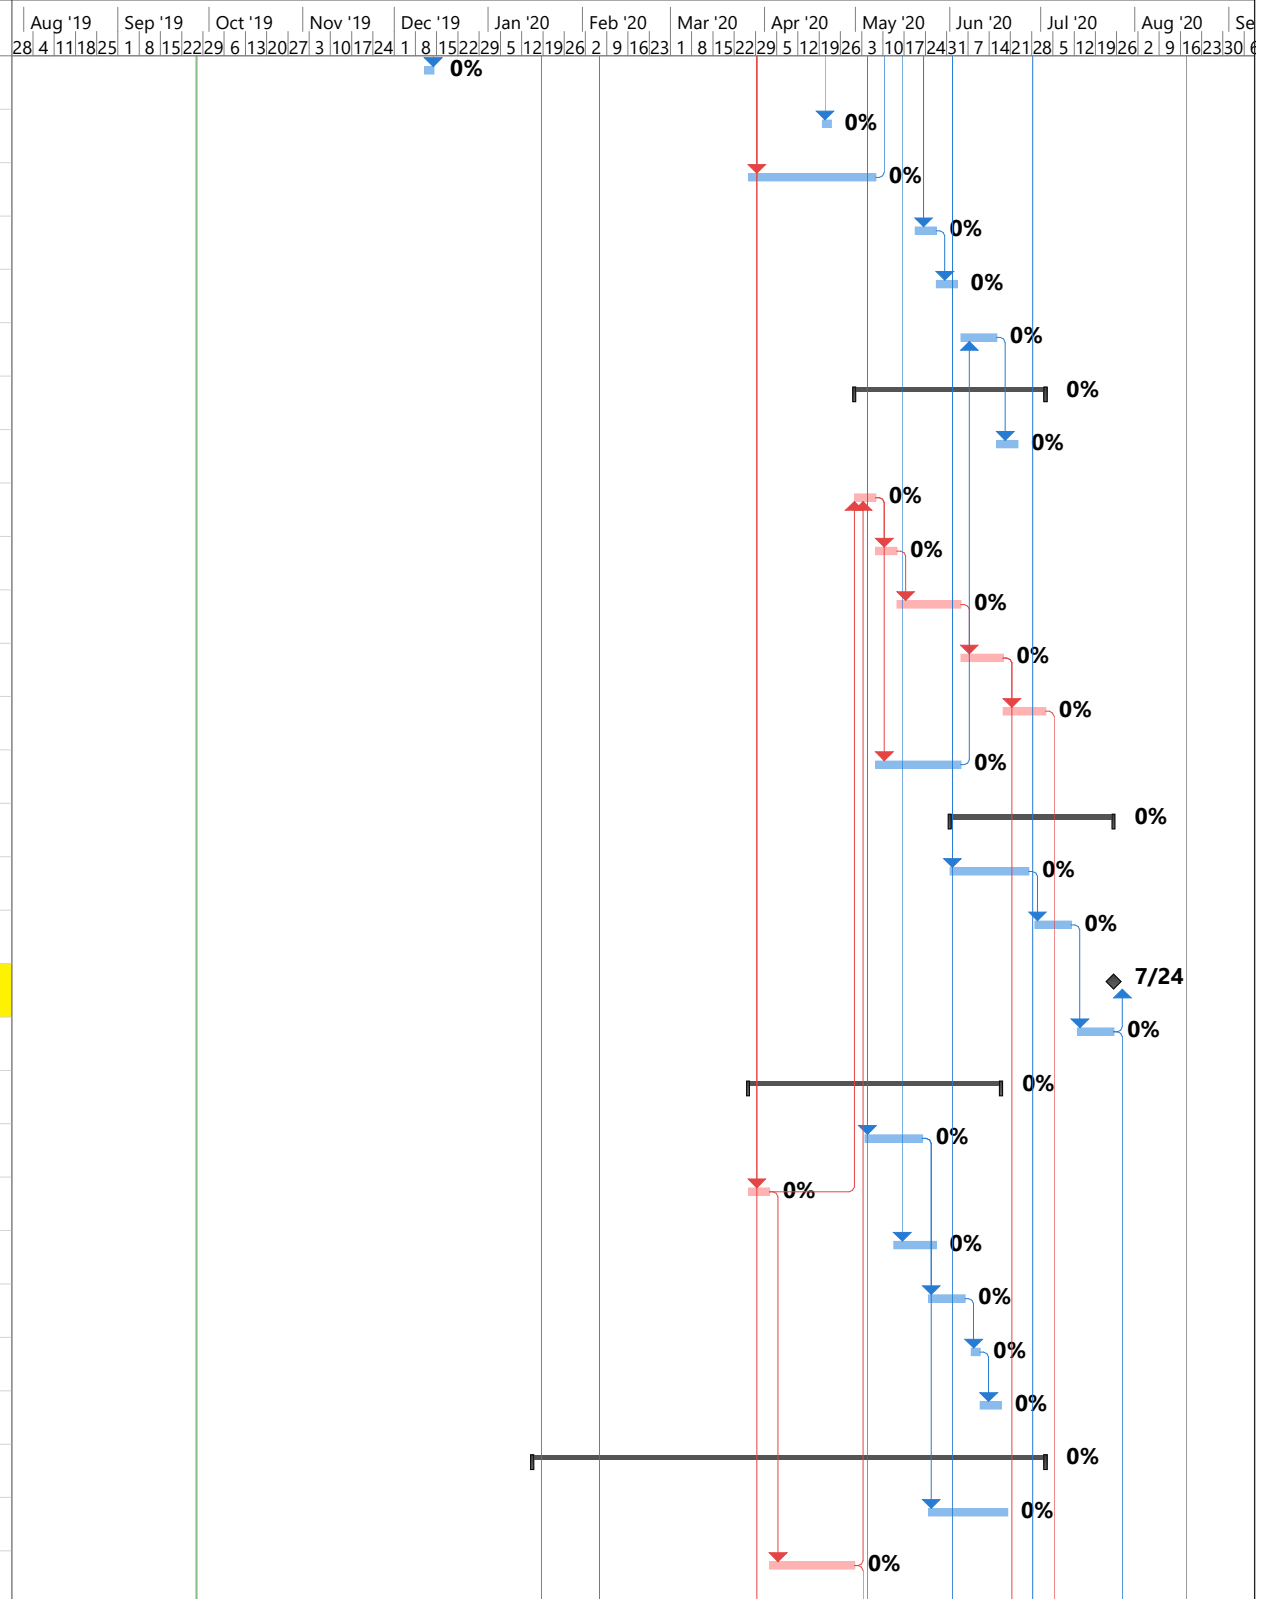



F.A. NUNNELLY
GENERAL CONTRACTOR

ID	Task Name	Start	Finish	Aug '19	Sep '19	Oct '19	Nov '19	Dec '19	Jan '20	Feb '20	Mar '20	Apr '20	May '20	Jun '20	Jul '20	Aug '20	Se
156	Pull wire in conduit and set area transformers	Wed 1/15/20	Wed 2/5/20							0%							
157	Install and terminate electrical devices	Thu 4/30/20	Thu 5/21/20														
158	Make electrical terminations for HVAC equipment	Thu 5/21/20	Mon 5/25/20														
159	UG Conduits for Site Lighting	Wed 1/15/20	Wed 1/29/20							0%							
160	Install light fixtures - test and clean	Thu 6/18/20	Thu 7/2/20														
161	Heating and Ventilating - AC	Thu 3/26/20	Tue 7/28/20														
162	Set equipment in mechanical room	Mon 6/1/20	Fri 6/12/20														
163	Rough-in mechanical in masonry walls	Mon 5/4/20	Fri 5/29/20														
164	Rough-in mechanical in drywall walls	Thu 3/26/20	Thu 4/9/20														
165	Set HVAC trim and test and balance system	Thu 7/2/20	Tue 7/28/20														
166	Final Clean-up and Occupancy	Tue 7/28/20	Mon 8/10/20														
167	Remove debris from building and do rough clean	Tue 7/28/20	Mon 8/3/20														
168	Final Clean-up	Mon 8/3/20	Mon 8/10/20														
169	Substantial completion date	Mon 8/10/20	Mon 8/10/20														
170	Complete Final Inspections	Mon 7/27/20	Mon 8/17/20														
171	Complete elevator inspection and certification	Mon 7/27/20	Wed 7/29/20														
172	Perform architect's inspection	Mon 8/10/20	Thu 8/13/20														
173	Perform local building agency inspection	Thu 8/13/20	Mon 8/17/20														
174	Perform Fire Marshal's inspection	Mon 8/3/20	Tue 8/4/20														
175	SUBSTANTIAL COMPLETION - FIELD AND TRACK	Thu 6/25/20	Thu 6/25/20														
176	Complete punch list items from all inspections	Mon 8/3/20	Mon 8/10/20														
177	CERTIFICATE OF OCCUPANCY - SUBSTANTIAL COMPLETION OF CONCESSIONS, TICKETS, ETC.	Mon 8/17/20	Mon 8/17/20														
178	Issue final completion documents including warranties	Mon 8/17/20	Mon 8/17/20														

